




Monterey Regional Airport

SAFETY ENHANCE PROGRAM 3-MONTH PROSPECTIVE PLAN


IN THE PRESENTATION

- Landside Construction
 - Phasing Plan/Current construction
 - 3 month look ahead
- Replacement Terminal Construction
 - Construction Site Progress
 - Current Construction
 - 3 month look ahead

CURRENT PHASING PLAN

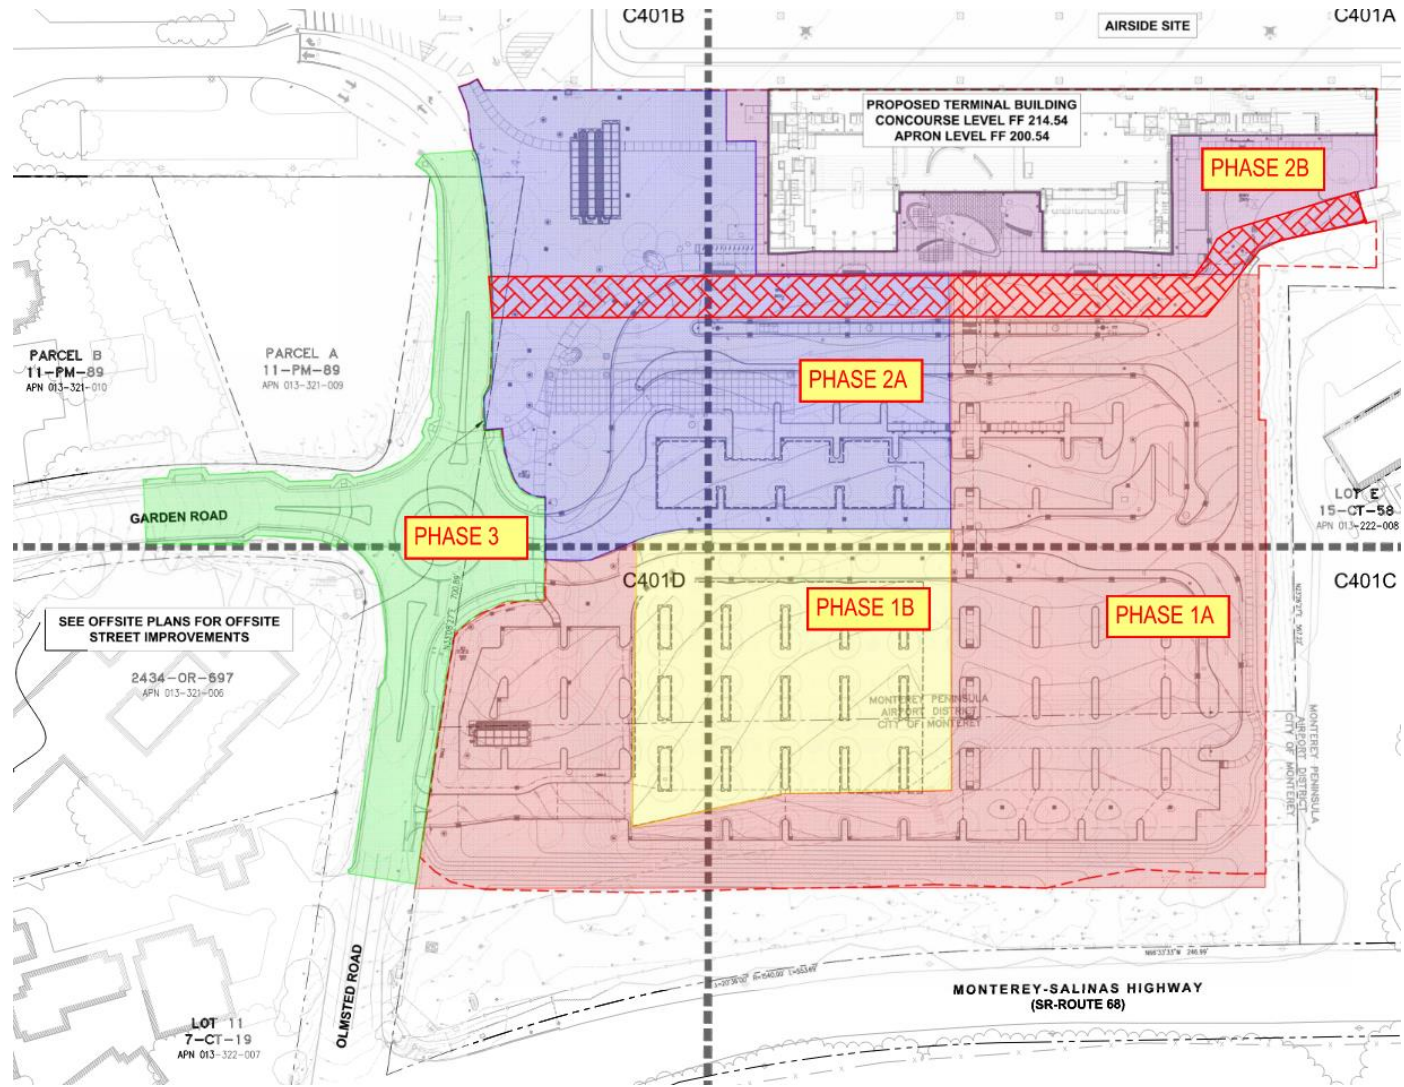

PARKING LOT INFILTRATION BASIN

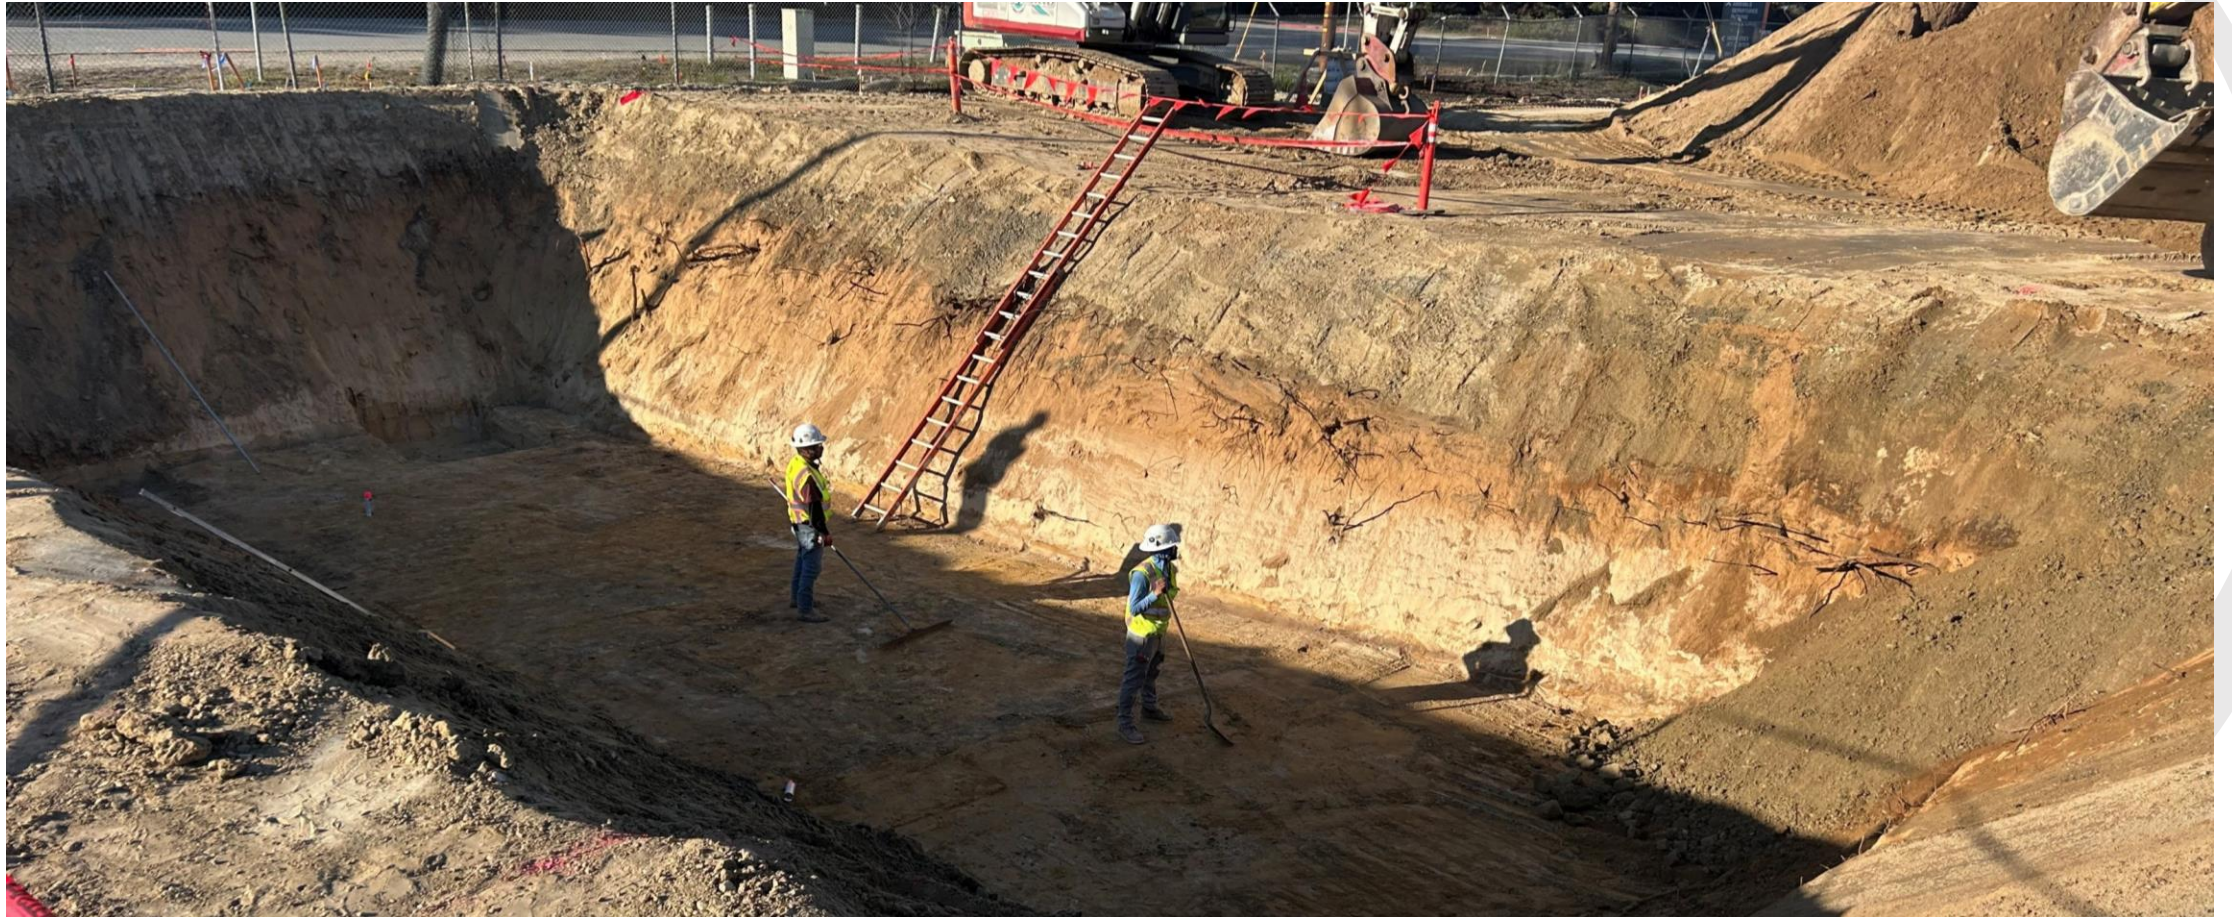

LANDSIDE IMPROVEMENTS PHASE 1

- February 2026
 - Rough grading of long-term parking lot Phase 1A
 - Underground utility installation continues
 - Install storm water infiltration basin
- March 2026
 - Roundabout construction to begin with underground stormwater facilities
 - Approx. 4 Month phased construction to minimize traffic impact.
 - Soil stabilization, grading and paving to continue in Phase 1A
- April 2026
 - Roundabout construction continues
 - Concrete curb and planter installation
 - PARCS equipment site prep

South Aerial View



Monterey Regional Airport New Terminal Facility | Design Presentation | May 30, 2024




REPLACEMENT TERMINAL – DRONE 9/11/25



REPLACEMENT TERMINAL – DRONE 1/28/26



REPLACEMENT TERMINAL PROGRESS

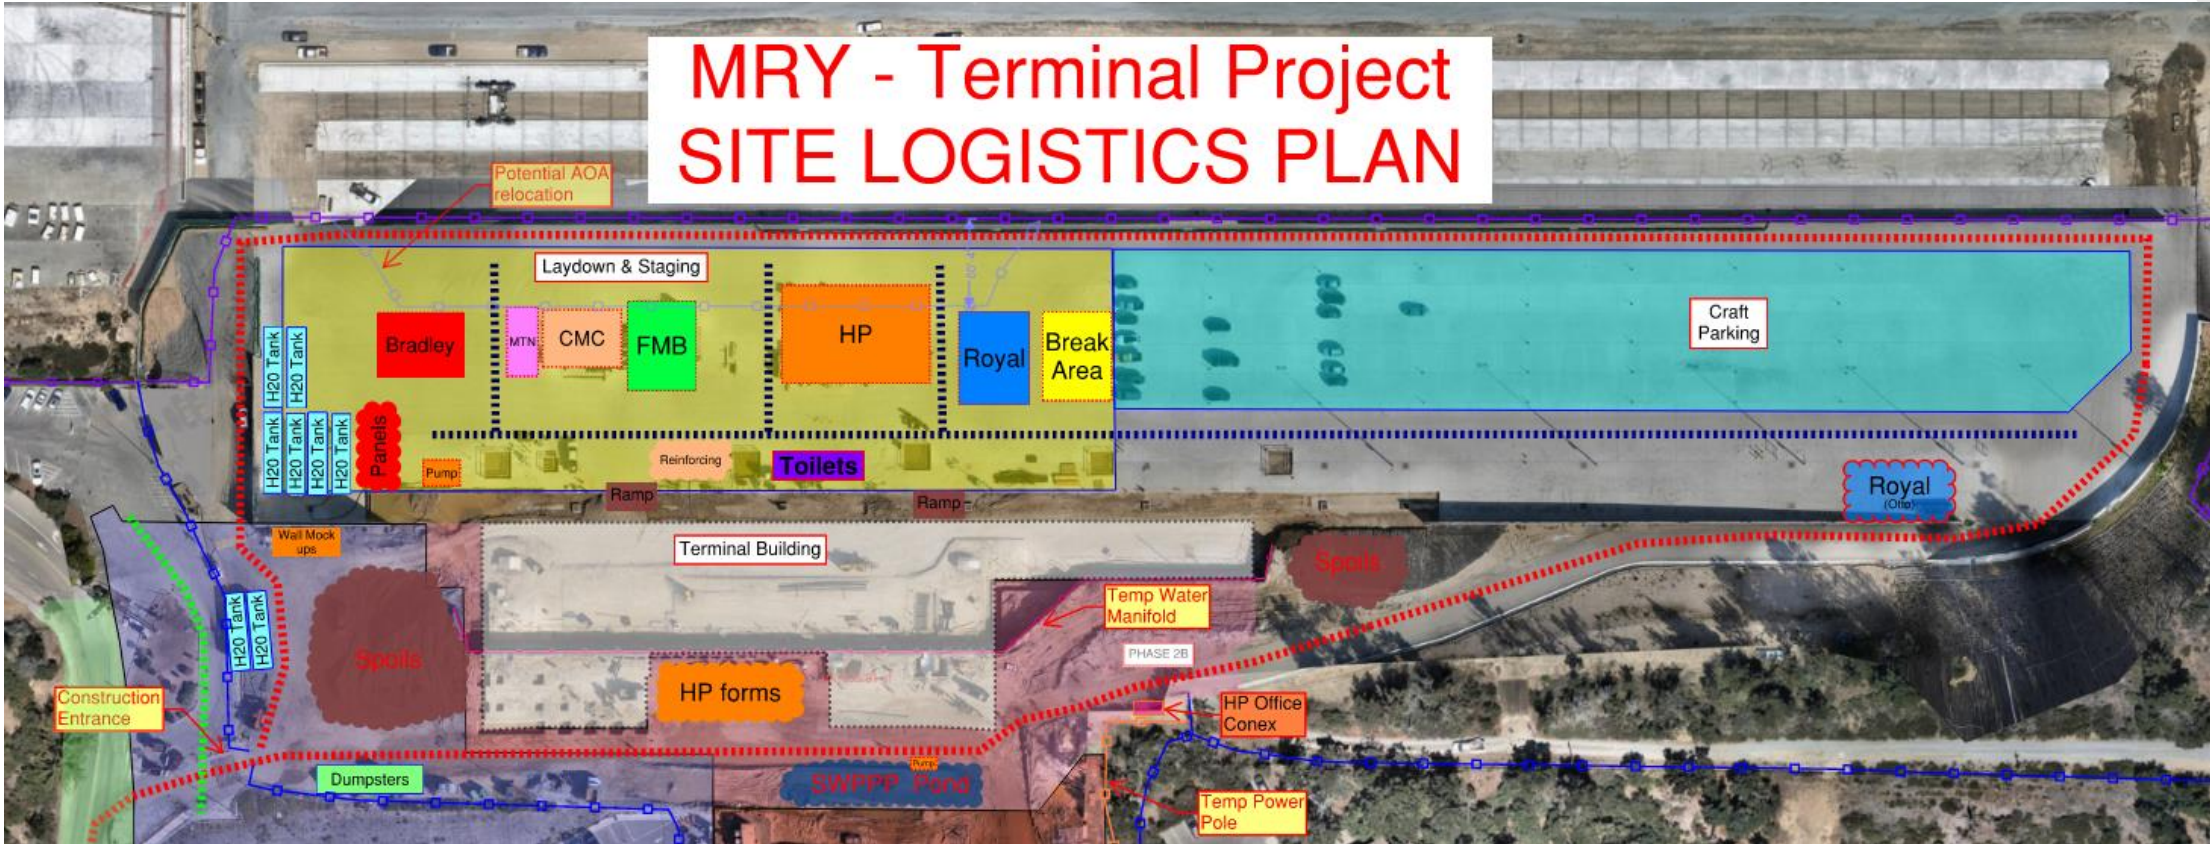

REPLACEMENT TERMINAL PROGRESS

- 360 Site View of Terminal
 - <https://youtu.be/atJMuInWNFE>
- Drone Flight of Arrivals Concrete Place
 - <https://youtu.be/ws7vk7zj8Kg>



REPLACEMENT TERMINAL PROGRESS



REPLACEMENT TERMINAL

Baggage drop at Departures



Foundation excavation concrete placement




Overcoming weather – 1 week later, place Concrete



REPLACEMENT TERMINAL

- February 2026
 - Foundation/Underground Utilities/Wall Prep & Forming
- March 2026
 - Finalized GMP 4
 - Foundations/Underground Utilities/Shotcrete walls/Slab on Grade
- April 2026
 - Underground Utilities
 - Steel/Decking
- May 2026
 - Steel/Decking

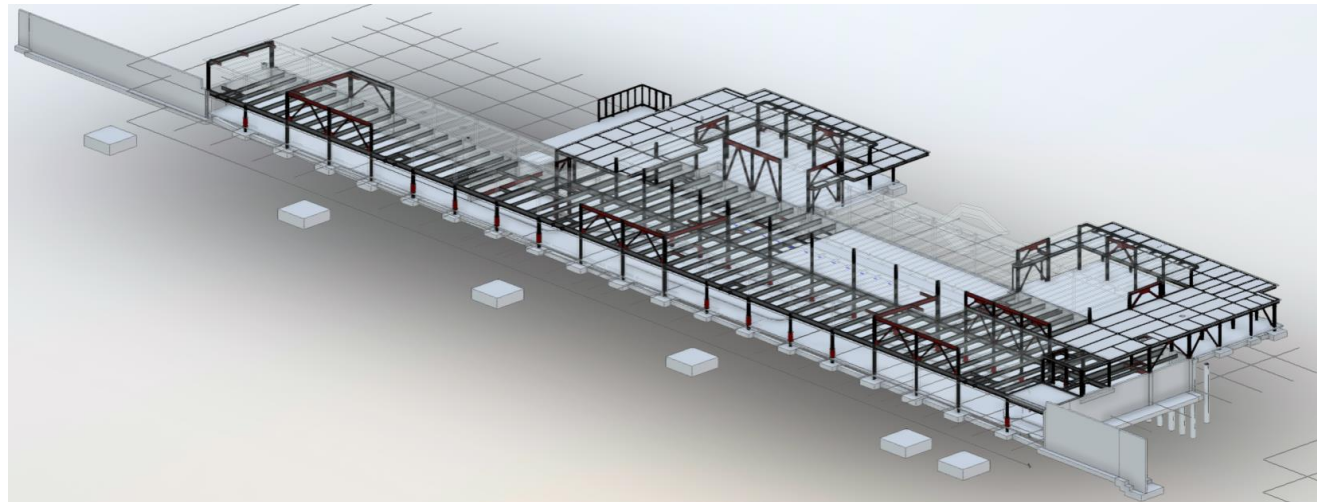



MONTEREY
REGIONAL AIRPORT

Thank you!

FLY LOCAL. FLY MRY.
